

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	2009				2010				2011				2012				2013				2014				2015				2016				2017																																																				
							M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M

Program Wide						
DA0010	Design Approval Phase 2	0	14MAY09A		14MAY09A	
DA0020	Critical Cross Sections	20	14MAY09	11JUN09	01JUN17	28JUN17
DA0030	MOT Report	110	14MAY09	20OCT09	26JAN17	28JUN17
DA0040	Barrier Warrant Analysis	40	14MAY09	10JUL09	04MAY17	28JUN17
DA0050	LS/Erosion Control Reports	20	14MAY09	11JUN09	01JUN17	28JUN17

VE Review						
VE0010	Ramp B	30	14MAY09*	25JUN09	14MAY09*	25JUN09
VE0020	Ramp C	30	14MAY09	25JUN09	14MAY09	25JUN09
VE0030	I-57 SB Mainline	30	14MAY09*	25JUN09	14MAY09*	25JUN09
VE0040	Tolling Options	30	14MAY09*	25JUN09	14MAY09*	25JUN09
VE0050	VE Complete	0		25JUN09		21JUL09

I-294 Utilities						
294UT0010	ROW Acquisition	621	01JUL09*	30DEC11	01JUL09*	30DEC11
294UT0020	Utility Relocation	558	03JAN11*	29MAR13	03JAN11*	29MAR13
294UT0030	Fiber Optic Relocation	558	03JAN11*	29MAR13	03JAN11*	29MAR13


I-57 Utilities						
57UT0010	ROW Acquisition	621	01JUL09*	30DEC11	01JUL09*	30DEC11
57UT0020	Utility Relocation	558	03JAN11*	29MAR13	03JAN11*	29MAR13
57UT0030	Fiber Optic Relocation	558	03JAN11*	29MAR13	03JAN11*	29MAR13

I-57 over I-294						
BR570010	Preliminary Plans 60%	40	26JUN09	21AUG09	22JUL09	16SEP09
BR570020	Agency Review 60%	20	24AUG09	21SEP09	17SEP09	15OCT09
BR570030	Pre-Final Plans 95%	20	22SEP09	20OCT09	16OCT09	13NOV09
BR570040	Agency Review 95%	20	21OCT09	18NOV09	16NOV09	15DEC09
BR570050	Submit Final Plans	1	19NOV09	19NOV09	16DEC09	16DEC09
BR570060	Agency Review Final Plans	10	19NOV09	04DEC09	16DEC09	30DEC09
BR570070	Final Revisions/Advertisement Authorization	10	19NOV09	04DEC09	16DEC09	30DEC09
BR570080	Advertise Bid Plans	21	07DEC09	06JAN10	31DEC09	01FEB10
BR570140	Pre-Bid Meeting	1	21DEC09	21DEC09	01FEB10	01FEB10
BR570090	Bid Opening	0	07JAN10		02FEB10	
BR570100	DSE Bid Evaluation	15	07JAN10	28JAN10	02FEB10	24FEB10
BR570110	Board Award	0	25FEB10		25FEB10	
BR570120	Notice to Proceed/Contract Initiation	30	25FEB10	07APR10	25FEB10	07APR10
BR570130	Construction	307	08APR10	30JUN11	08APR10	30JUN11

Ramp B Northbound						
B0010	Preliminary Plans 60%	70	26JUN09	05OCT09	31DEC09	13APR10
B0020	Agency Review 60%	20	06OCT09	03NOV09	14APR10	11MAY10
B0030	Pre-Final Plans 95%	25	04NOV09	11DEC09	12MAY10	16JUN10
B0040	Agency Review 95%	20	14DEC09	12JAN10	17JUN10	15JUL10
B0050	Submit Final Plans	1	13JAN10	13JAN10	16JUL10	16JUL10
B0060	Agency Review Final Plans	10	13JAN10	27JAN10	16JUL10	29JUL10
B0070	Final Revisions/Advertisement Authorization	10	13JAN10	27JAN10	16JUL10	29JUL10
B0080	Advertise Bid Plans	21	28JAN10	01MAR10	21OCT10	22NOV10
B0140	Pre-Bid Meeting	1	11FEB10	11FEB10	22NOV10	22NOV10
B0090	Bid Opening	0	02MAR10		23NOV10	
B0100	DSE Bid Evaluation	15	02MAR10	22MAR10	23NOV10	15DEC10
B0110	Board Award	0	25MAR10		16DEC10	
B0120	Notice to Proceed/Contract Initiation	30	25MAR10	05MAY10	21JAN11	07MAR11
B0130	Construction	445	08MAR11	17DEC12	08MAR11	17DEC12

Ramp M Southbound						
M0010	Preliminary Plans 60%	70	26JUN09	05OCT09	01FEB10	11MAY10
M0020	Agency Review 60%	10	06OCT09	20OCT09	12MAY10	25MAY10
M0030	Pre-Final Plans 95%	25	21OCT09	25NOV09	26MAY10	30JUN10
M0040	Agency Review 95%	10	30NOV09	11DEC09	01JUL10	15JUL10
M0050	Final Submittal Plans 100%	1	14DEC09	14DEC09	16JUL10	16JUL10
M0060	Agency Review 100%	10	14DEC09	28DEC09	16JUL10	29JUL10
M0070	Final Revisions/Advertisement Authorization	10	14DEC09	28DEC09	16JUL10	29JUL10
M0080	Advertise Bid Plans	21	29DEC09	28JAN10	07JAN13	04FEB13
M0140	Pre-Bid Meeting	1	13JAN10	13JAN10	04FEB13	04FEB13
M0090	Bid Opening	0	29JAN10		05FEB13	
M0100	DSE Bid Evaluation	15	29JAN10	22FEB10	05FEB13	27FEB13
M0110	Board Award	0	25FEB10		28FEB13	
M0120	Notice to Proceed/Contract Initiation	30	25FEB10	07APR10	28FEB13	10APR13
M0130	Construction	362	05JUL11	17DEC12	11APR13	18SEP14

Kedzie Ave over I-57						
K0010	Preliminary Plans 60%	68	06OCT09	15JAN10	25JUN15	30SEP15
K0020	Agency Review	20	19JAN10	17FEB10	01OCT15	29OCT15
K0030	Pre-Final 95%	20	18FEB10	17MAR10	30OCT15	01DEC15
K0040	Agency Review 95%	20	18MAR10	14APR10	02DEC15	30DEC15
K0050	Submit Final Plans	1	15APR10	15APR10	31DEC15	31DEC15
K0060	Agency Review 100%	10	15APR10	28APR10	31DEC15	14JAN16
K0070	Final Revisions/Advertisement Authorization	10	15APR10	28APR10	31DEC15	14JAN16
K0080	Advertise Bid Plans	21	15APR10	13MAY10	31DEC15	01FEB16
K0140	Pre-Bid Meeting	1	29APR10	29APR10	01FEB16	01FEB16
K0090	Bid Opening	0	14MAY10	13MAY10	02FEB16	01FEB16
K0130	DSE Bid Evaluation	15	14MAY10	04JUN10	02FEB16	24FEB16
K0100	Board Award	0	24JUN10		25FEB16	

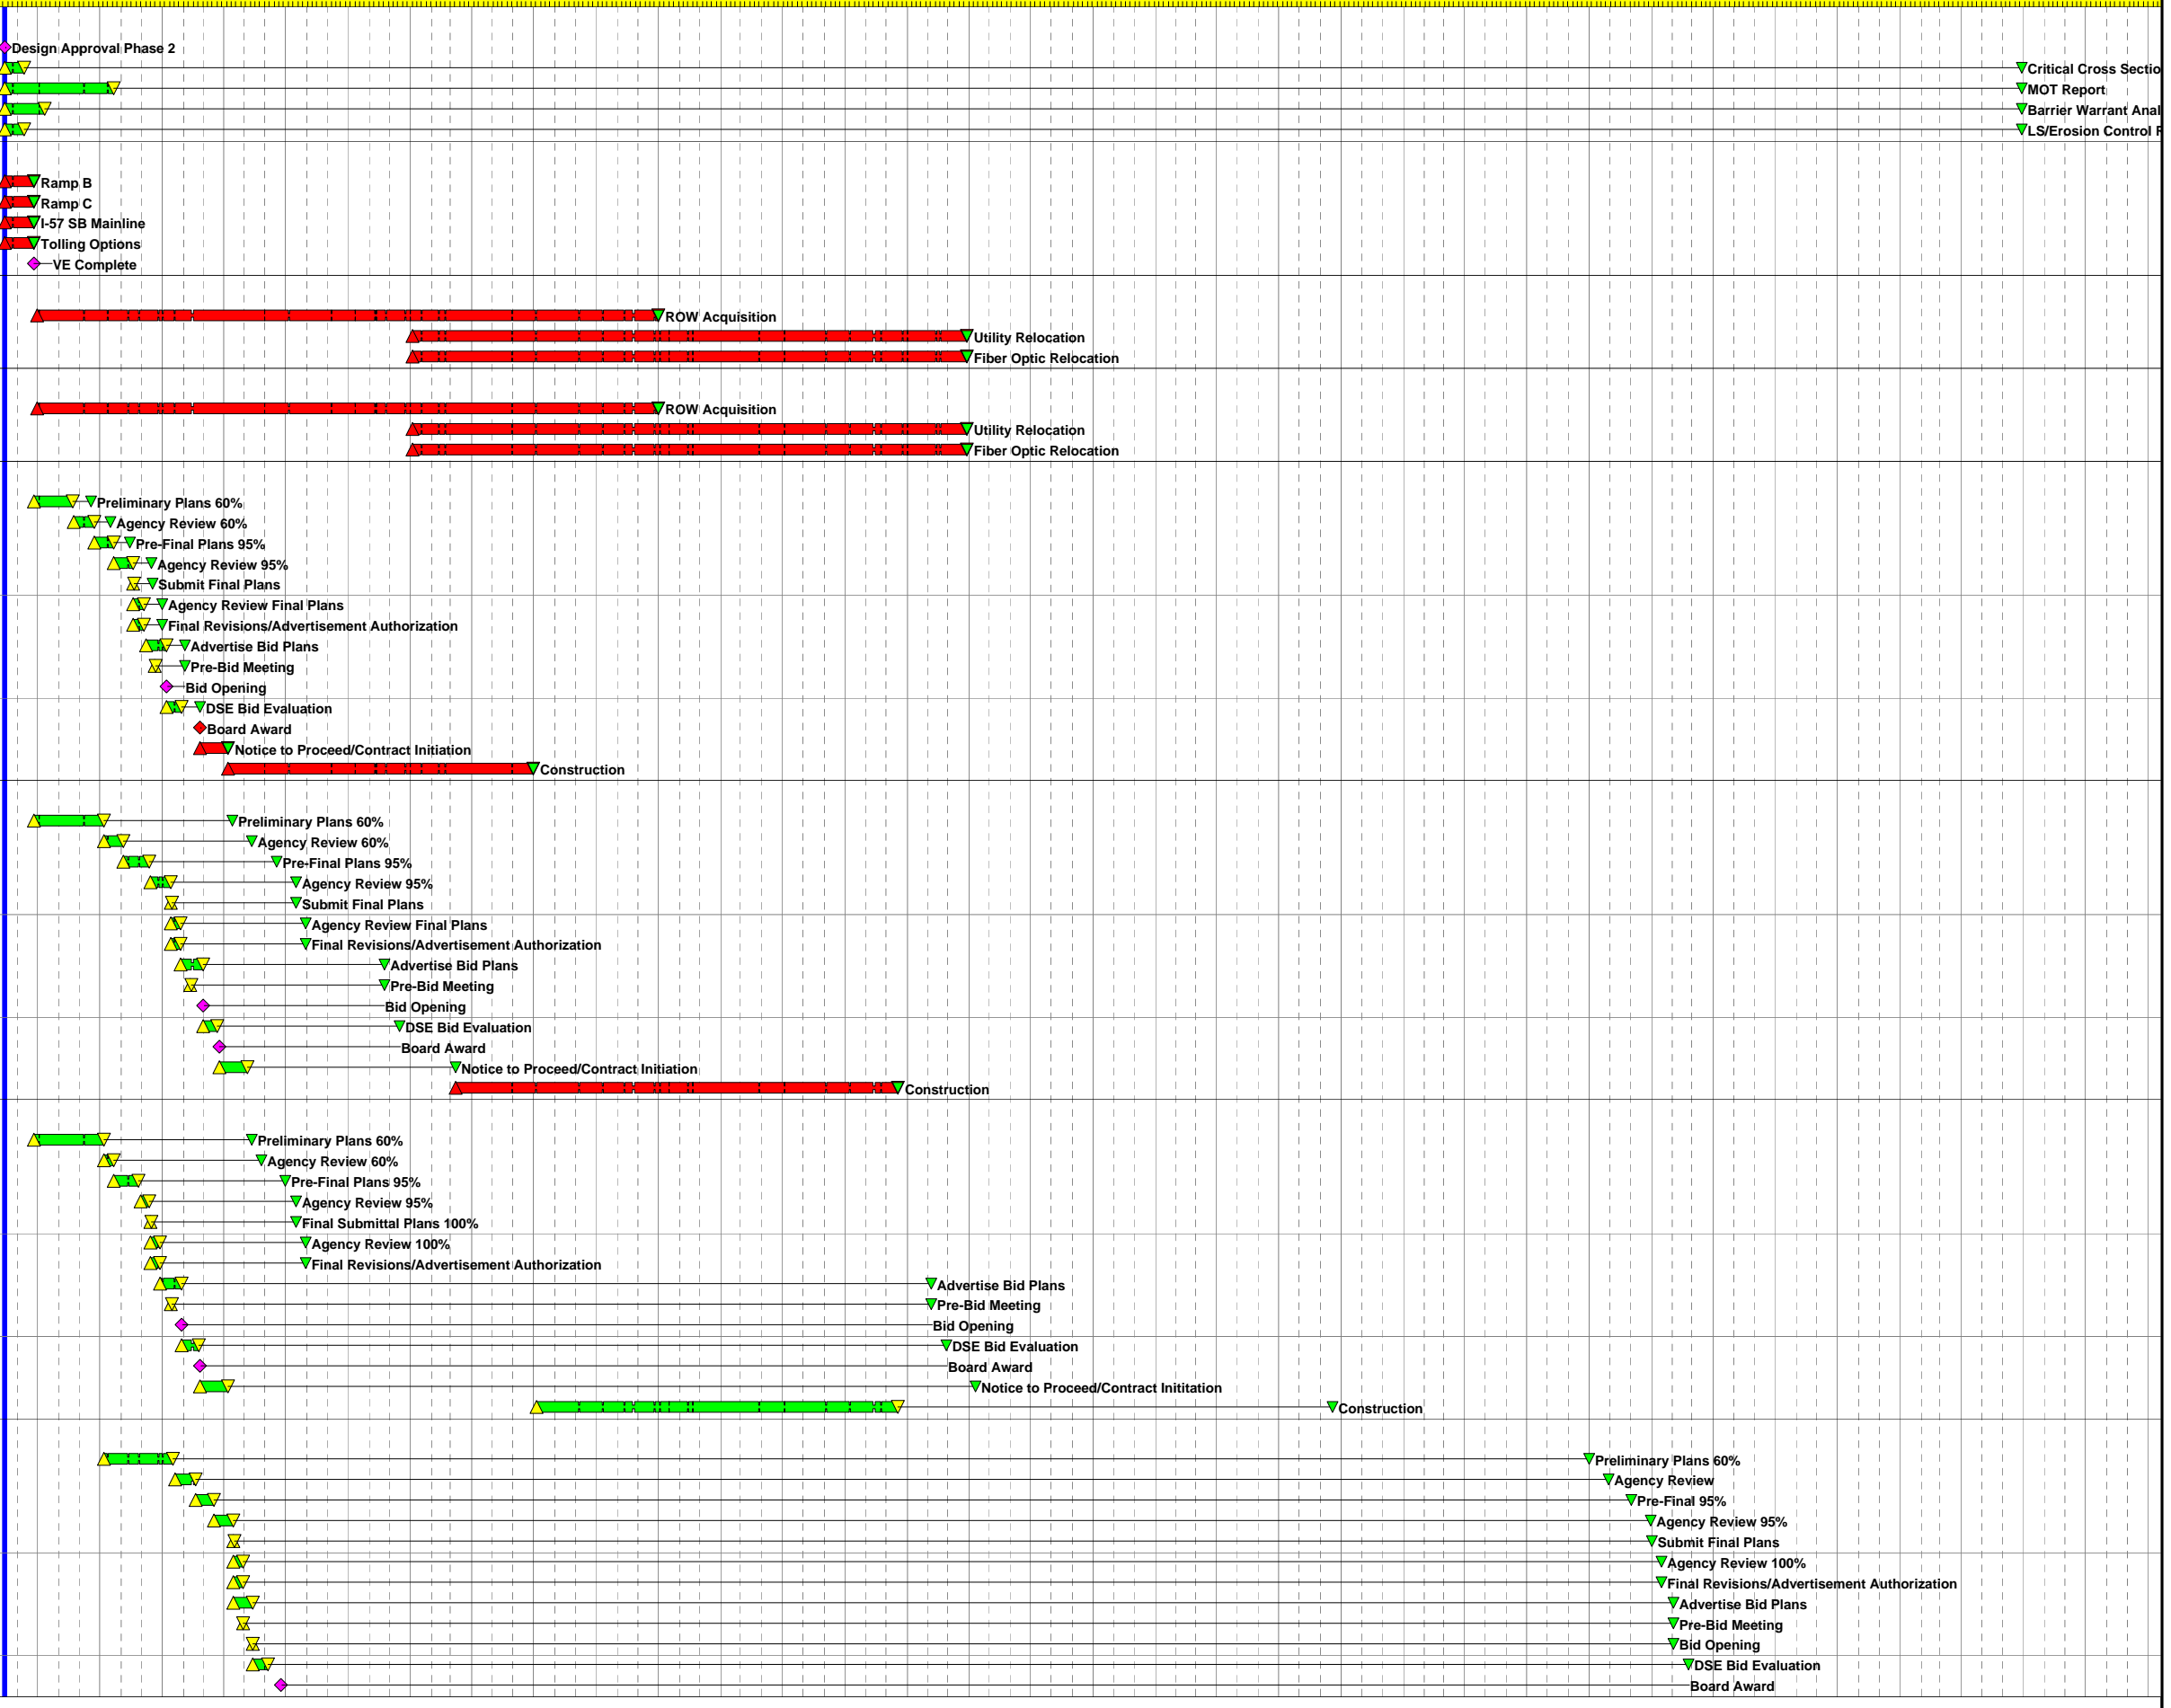

Start Date	01MAY09	Legend: Early Bar	1294	Sheet 1 of 3	Date	Revision	Checked	Approved
Finish Date	28JUN17	Legend: Float Bar						
Data Date	14MAY09	Legend: Progress Bar						
Run Date	09JUL09 13:43	Legend: Critical Activity						

Interchange at I-294 & I-57 Design
Classic Schedule Layout

© Primavera Systems, Inc.

